


ACAD 16.1s (LMS Tech)
03/26/08 DB:13:12
RUM02025
E1
03/26/08

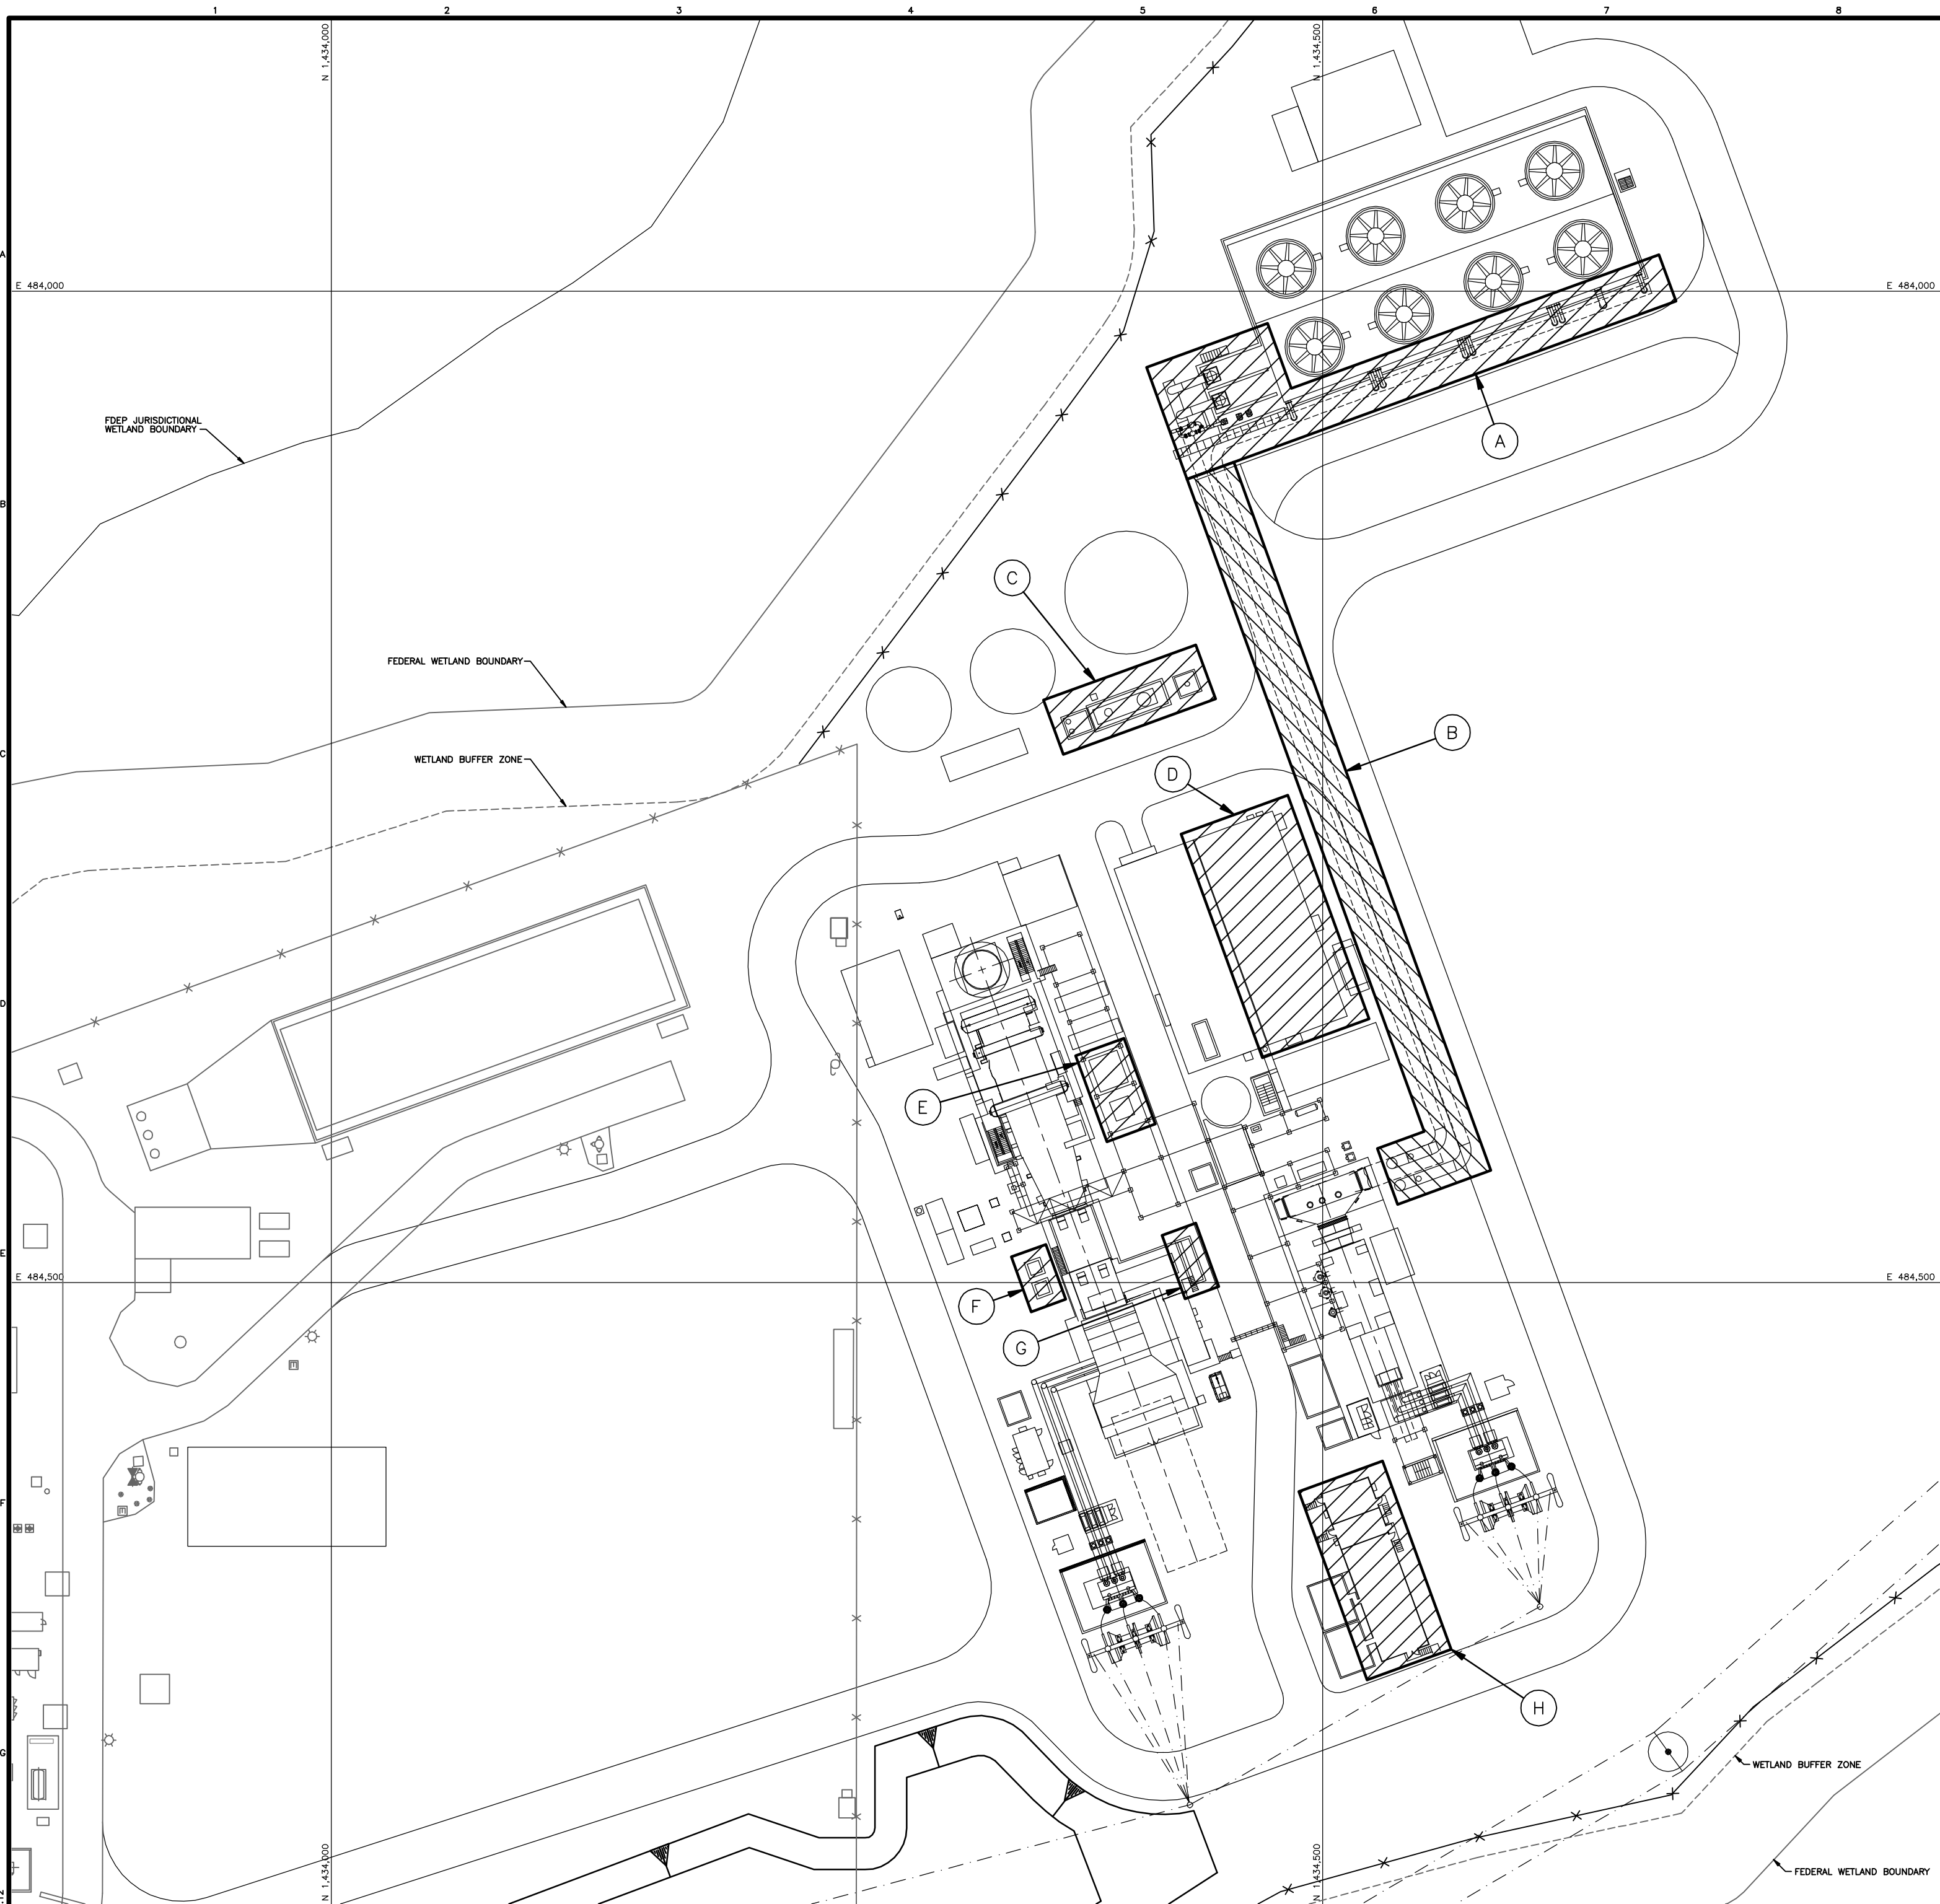

DEWATERING SCHEDULE

DEWATERING AREA	DEWATERING AREA DESCRIPTION	APPROXIMATE DURATION DEWATERING WILL BE IN PLACE	REQUIRED DEWATER DEPTH (FEET BELOW GROUND SURFACE)
A	COOLING TOWER AND CIRCULATING WATER PUMP PIT	WEEKS 1 THRU 10	14
B	UNDERGROUND CIRCULATING WATER PIPE	WEEKS 1 THRU 6	14
C	OIL/WATER SEPARATOR AND WASTEWATER SUMP	WEEKS 7 THRU 10	15
D	MISCELLANEOUS SERVICE BUILDING VAULT	WEEKS 7 THRU 10	8
E	BLOWDOWN TANK SUMP AND BLOWDOWN SUMP	WEEKS 11 THRU 16	10
F	WASHWATER TANK	WEEKS 11 THRU 13	8
G	ACCESSORY MODULE TRENCH AND SUMP	WEEKS 14 THRU 16	8
H	ELECTRICAL EQUIPMENT BUILDING	WEEKS 17 THRU 21	8

LEGEND

-----	WETLAND BUFFER ZONE	-----	OVERHEAD TRANSMISSION LINE
-----	FDEP JURISDICTIONAL WETLAND BOUNDARY	XXXXX	FENCE LINE
[Hatched Box]	GOPHER TORTOISE HABITAT		
①	DEWATERING AREA		

NOTES


- SEE DRAWING 147651-4STA-S1001 FOR SITE ARRANGEMENT.
- DEWATERING SHALL BE COMPLETED WITH A SERIES OF WELLPOINTS INSTALLED AROUND THE PERIMETER OF EXCAVATION. DISCHARGE FROM DEWATERING ACTIVITIES SHALL BE DIRECTED TO UNIT 3 AND 4 STORM WATER POND.

**FOR PERMITTING
PURPOSE ONLY
APPROVED FOR
CONSTRUCTION**

ENGINEER	JMS	DRAWN	MRR
CHECKED	JMS	DATE	04/01/2008

FLORIDA MUNICIPAL POWER AGENCY CANE ISLAND POWER PARK UNIT 4	PROJECT 147651-DS-0110	DRAWING NUMBER	REV 0
DEWATERING PLAN	CODE	AREA	

0	04/01/2008	ISSUED FOR CONSTRUCTION	MRJMS/MSJ/MSJ
NO.	DATE	REVISIONS AND RECORD OF ISSUE	BY/DESIGNER/DATE



I HEREBY CERTIFY THAT THIS DOCUMENT WAS PREPARED BY ME OR UNDER MY DIRECT SUPERVISION AND THAT I AM A QUALIFIED REGISTERED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF FLORIDA.
SIGNED: _____
DATE: _____ REG. NO. _____

BLACK & VEATCH CORPORATION	ENGINEER	JMS	DRAWN	MRR
	CHECKED	JMS	DATE	04/01/2008
