




PROJECT NUMBER 338884.FL	WELL NUMBER MW-7S	SHEET 1	OF 1
WELL COMPLETION DIAGRAM			

PROJECT : PEF COLA LOCATION : Levy Nuclear Plant Site

DRILLING CONTRACTOR : Prosonic / Head Driller F Kraus

DRILLING METHOD AND EQUIPMENT USED : Rotosonic 4"/6" SR109

WATER LEVELS : See well development log MW-7S START : 2/1/07 END : 2/1/07 LOGGER : Faroute

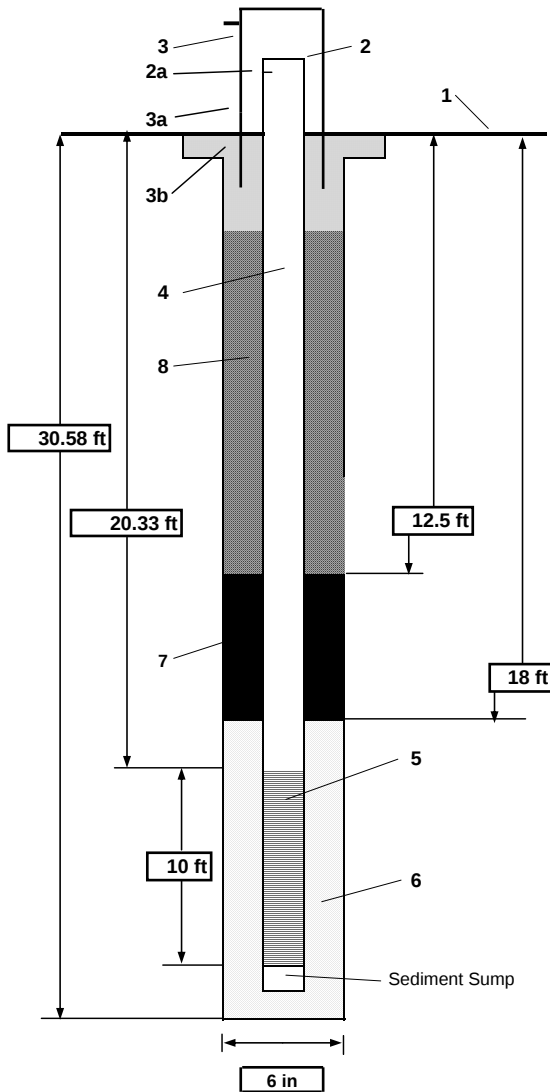

1- Ground elevation at well	44.22 ft.
2- Top of casing elevation	46.91 ft.
a) vent hole?	N/A
3- Wellhead protection cover type	Metal Locking Protective Casing
a) weep hole?	N/A
b) concrete pad dimensions	3 ft x 3ft
4- Diameter/type of well casing	2" sch 40 PVC
5- Type/slot size of screen	2" sch 40 PVC 10-slot
6- Type screen filter	20-30 mesh/pea gravel sand
a) Quantity used	5 bags
7- Type of seal	Bentonite Pellets (3/8")
a) Quantity used	1 bags
8- Grout	
a) Grout mix used	Cement-Bentonite
b) Method of placement	Tremie Method
c) Vol. of well casing grout	Not measured
Development method	Surge block and submersible pump
Development time	2 hour 15 minutes
Estimated purge volume	170 gallons
Comments	
	Total Well Depth (BTOC) = 33.27 ft
	Final Well Development Field Parameters:
	pH = 7.05 , Conductivity = 0.464 µs/cm, T = 23.10 °C

NOTE: Diagram is not to scale.
