




PROJECT NUMBER 338884.FL	WELL NUMBER MW-16D	SHEET 1	OF 1
WELL COMPLETION DIAGRAM			

PROJECT : PEF COLA LOCATION : Levy Nuclear Plant Site
 DRILLING CONTRACTOR : Prosonic / Head Driller F Kraus
 DRILLING METHOD AND EQUIPMENT USED : Rotosonic 4"/6" SR109
 WATER LEVELS : See well development log MW-16D START : 2/11/07 END : 2/12/07 LOGGER :

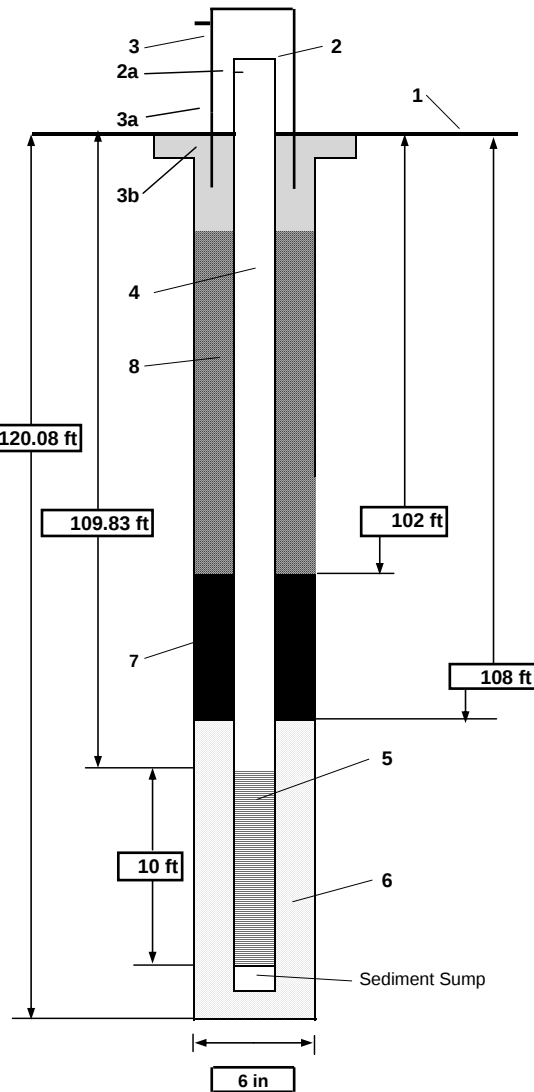

1- Ground elevation at well	43.34 ft
2- Top of casing elevation	46.01 ft
a) vent hole?	N/A
3- Wellhead protection cover type	Metal Locking Protective Casing
a) weep hole?	N/A
b) concrete pad dimensions	3 ft x 3ft
4- Diameter/type of well casing	2" sch 40 PVC
5- Type/slot size of screen	2" sch 40 PVC 10-slot
6- Type screen filter	20-30 mesh/pea gravel sand
a) Quantity used	3.5 bags
7- Type of seal	Bentonite Pellets (3/8")
a) Quantity used	Not measured
8- Grout	
a) Grout mix used	Cement-Bentonite
	Bags not measured
b) Method of placement	Tremie Method
c) Vol. of well casing grout	Not measured
Development method	Surge block and submersible pump
Development time	2 hours 52 minutes
Estimated purge volume	600 gallons
Comments	
	Total Well Depth (BTOC) = 122.75 ft
	Final Well Development Field Parameters:
	pH = 6.97 , Conductivity = 0.436 μ S/cm, T = 22.40 $^{\circ}$ C

NOTE: Diagram is not to scale.
