




PROJECT NUMBER 338884.FL	WELL NUMBER OW-6	SHEET 1	OF 1
WELL COMPLETION DIAGRAM			

PROJECT : PEF COLA LOCATION : Levy Nuclear Plant Site

DRILLING CONTRACTOR : Prosonic / Head Driller F Kraus

DRILLING METHOD AND EQUIPMENT USED : Rotosonic 4"/6" SR109

WATER LEVELS : See well development log OW-6 START : 1/31/07 END : 1/31/07 LOGGER : Faroute

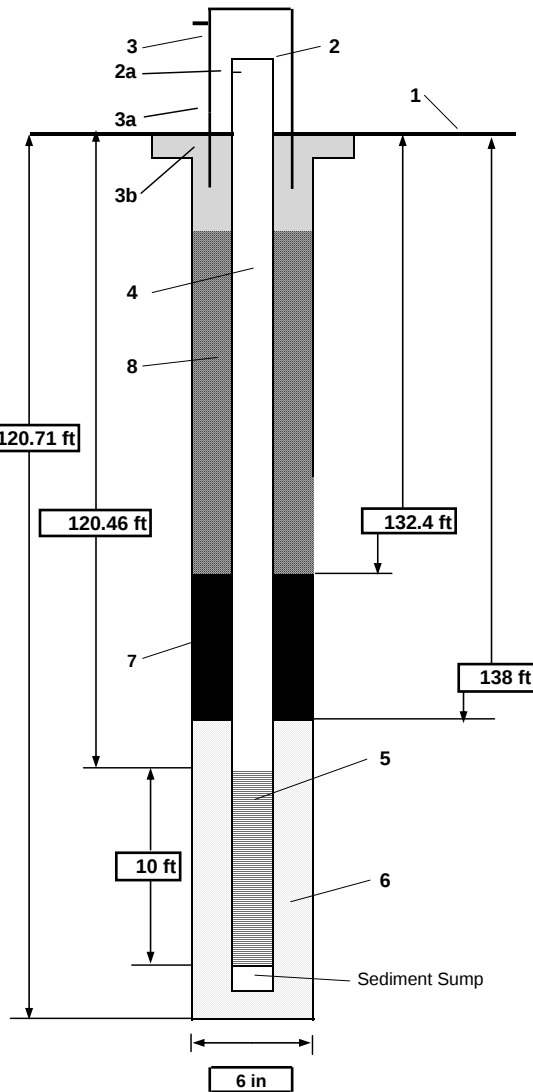

1- Ground elevation at well	43.15 ft
2- Top of casing elevation	45.53 ft
a) vent hole?	N/A
3- Wellhead protection cover type	Metal Locking Protective Casing
a) weep hole?	N/A
b) concrete pad dimensions	3 ft x 3ft
4- Diameter/type of well casing	2" sch 40 PVC
5- Type/slot size of screen	2" sch 40 PVC 10-slot
6- Type screen filter	20-30 mesh/pea gravel sand
a) Quantity used	6 bags
7- Type of seal	Bentonite Pellets (3/8")
a) Quantity used	Not Measured
8- Grout	
a) Grout mix used	Cement-Bentonite
	Bags not measured
b) Method of placement	Tremie Method
c) Vol. of well casing grout	1 gallon
Development method	Surge block and submersible pump
Development time	1 hour 25 minutes
Estimated purge volume	737.5 gallons
Comments	
	Total Well Depth (BTOC) = 79.11 ft
	Final Well Development Field Parameters:
	pH = 7.02, Conductivity = 0.368 µs/cm, T = 22.40 °C

NOTE: Diagram is not to scale.
